


Pike Branch Stream Restoration Project – Construction Status - Fall 2019




A. Intersection of Old Telegraph Road and Telegraph Road to 6232 Old Telegraph Road – Grading activities were completed in May 2019. Final native vegetation seedmix has been applied and tree saplings were planted. Additional streambank stabilization plantings will be installed prior to Spring 2020. Frogs, fish and other aquatic organisms were observed within pool areas of the stream during the site visit. Evidence of raccoon and white tail deer use of stream area was observed via footprints and scat.

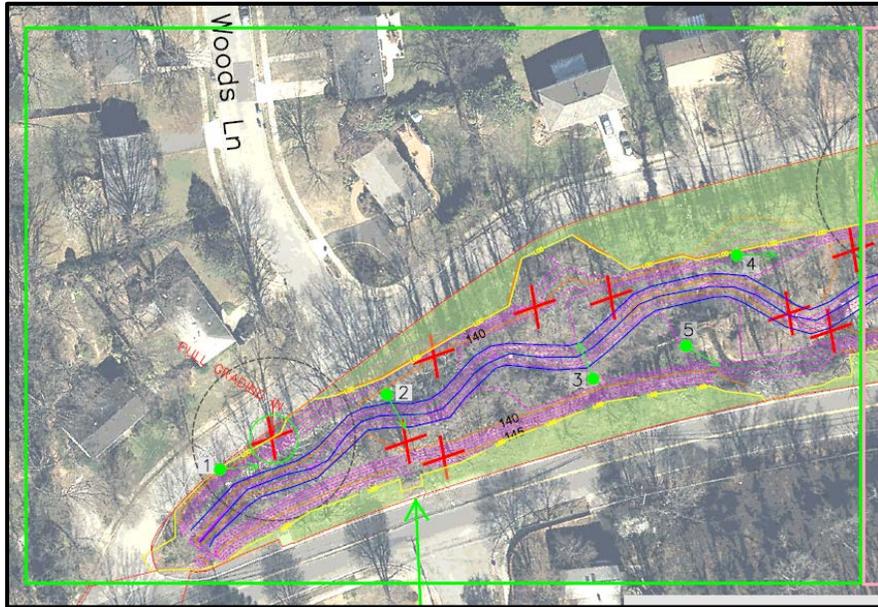

B. 6232 Old Telegraph Road to 6154 Old Telegraph Road – Grading activities were completed in August 2019. Final native vegetation seedmix has been applied. Streambank stabilization plantings will be installed prior to or in Spring 2020. Additional tree saplings will be planted in Spring 2020. Frogs, fish and other aquatic organisms were observed within upper pool areas of the stream during the site visit. Evidence of raccoon and white tail deer use of upper stream area was observed via footprints and scat.



C. 6154 Old Telegraph Road to 6136 Old Telegraph Road – Grading activities are anticipated to be completed by late Fall 2019 with final native vegetation seedmix being applied shortly after. Streambank stabilization plantings will be installed prior to or in Spring 2020. Additional tree saplings will be planted in Spring 2020.

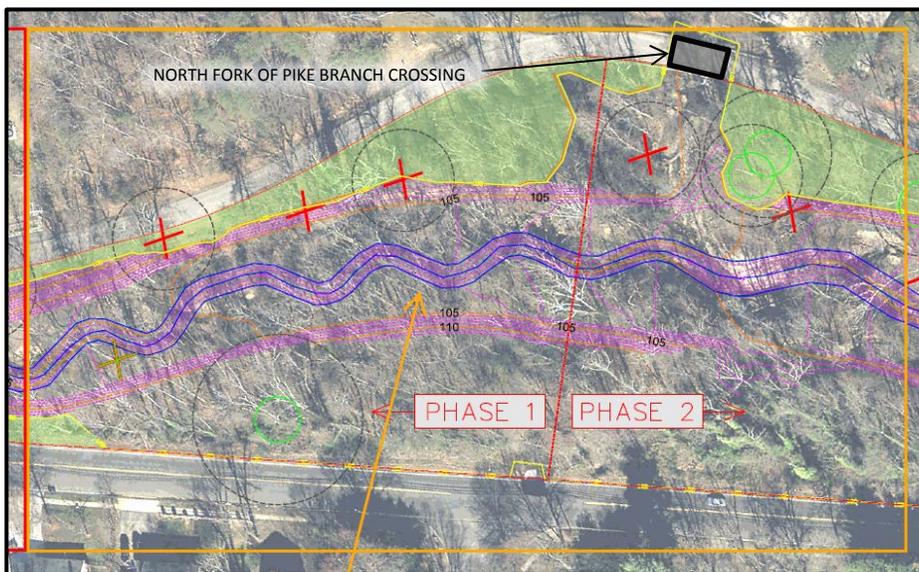

D. 6136 Old Telegraph Road to Hope United Church of Christ – Tree clearing activities have initiated to install the construction access road and Phase II staging area. Grading activities for Phase I, which terminates at the Old Telegraph Road Bridge are anticipated to be completed before the end of 2019. However, the Phase II staging area will remain in place until the completion of the project construction.

PHOTOSTATION 1 – April 2016



PHOTOSTATION 1 – August 2019



PHOTOSTATION 2 – April 2016



PHOTOSTATION 2 – August 2019



PHOTOSTATION 3 – April 2016



PHOTOSTATION 3 – August 2019



PHOTOSTATION 4 – April 2016



PHOTOSTATION 4 – August 2019



PHOTOSTATION 5 – February 2019



PHOTOSTATION 5 – August 2019



PHOTOSTATION 6 – April 2016



PHOTOSTATION 6 – August 2019



PHOTOSTATION 7 – April 2016



PHOTOSTATION 7 – August 2019



PHOTOSTATION 8 – April 2016



PHOTOSTATION 8 – August 2019



PHOTOSTATION 9 – April 2016



PHOTOSTATION 9 – October 2019



Additional Photos of Completed Areas



Additional Photos of Completed Areas



Additional Photos of Completed Areas



Additional Photos of Completed Areas



| LEGEND: | |
|---|----------------------------------|
|  | SPECIMEN TREES TO BE REMOVED |
|  | SPECIMEN TREES TO REMAIN |
|  | PROPOSED CONTOURS |
|  | PROPOSED STREAM CHANNEL LOCATION |
|  | VDOT ROW |
|  | TREE SAVE AREAS |
|  | LIMITS OF DISTURBANCE |
|  | PHOTOSTATION |
