



**Route 7 Widening
PARDON OUR DUST BRIEFING**

June 5th, 2013 – 6:00 PM

**Herndon High School Auditorium
700 Bennett Street
Herndon, VA 20170**

Tonight's Objective:

- **Introduction of the Construction Team**
- **Present Project Scope of Work**
- **Construction Elements**
 - **Sequence of Construction**
- **Answer your Questions**

Project Team

- Virginia Department of Transportation
- Contractor: Fort Myer Construction Corporation



ROUTE 7 WIDENING

Construction Team & Contact Information

Project updates will be posted on VDOT's website at:

http://www.virginiadot.org/projects/northernvirginia/route_7_widening_rolling_holly_to_reston_ave.asp


VDOT Construction Management contact information:

- Michael Gleasman, PE – Area Construction Engineer
 - (703) 259-1944 Michael.Gleasman@vdot.virginia.gov
- Tim Diliscia – Construction Manager
 - (540) 247-9953 Tim.Diliscia@vdot.virginia.gov
- Kevin Dellinger – Sr. Project Inspector
 - (571) 722-9600 Kevin.Dellinger@vdot.virginia.gov

Field office location (open during normal business hours):

- 46859 Harry Byrd Highway, Suite 301 (next to Koon's Ford Dealership)
- Phone Number: (571) 375-2465

Project Location

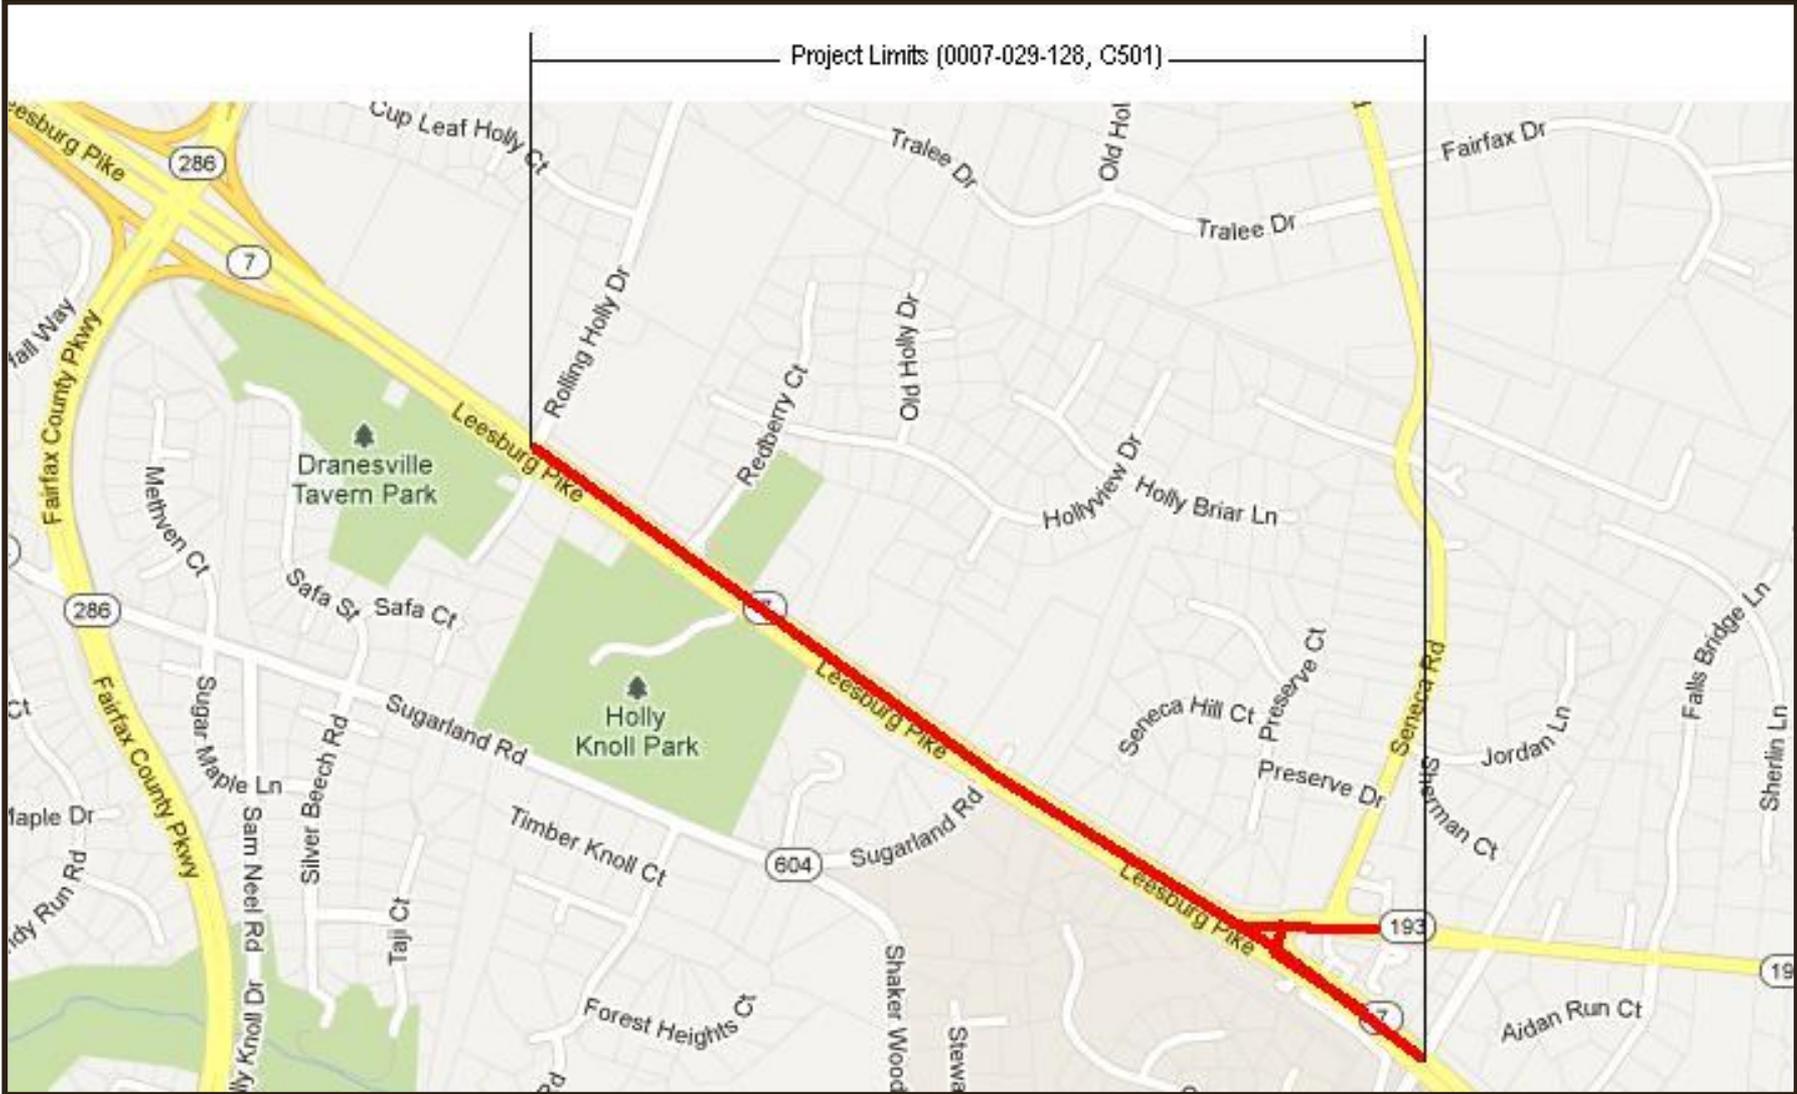

Project Overview

- Project Schedule
- Construction Impacts
- Public Notification
- Public Safety



Project Milestones

- **Contract Executed:** April 15th, 2013
- **Notice to Proceed Date:** May 14th, 2013
- **Start of Construction:** May 23rd, 2013
- **Substantial Completion:** November 12th, 2015
- **Final Completion:** December 16th, 2015

Project Information

New Signal at Redberry Ct. & Relocated Woody's Entrance

Projectwide - Over 25,000+ new trees, shrubs, and plantings

Retaining Walls

Intersection Improvements at Georgetown Pike

Begin Project Rolling Holly Dr.

Shared Use Path

End Project Reston Ave.

Utility Relocation and Construction Access


Due to current construction:

- Work at Seneca Road, Georgetown Pike and Rte. 7/Georgetown Pike intersection will not begin before August 15, 2013

Due to utility work:

- Work at EB/WB Rte. 7 from Rolling Holly Dr. to Dranesville Auto will not begin before July 1, 2013
- Work at EB/WB Rte. 7 from 700 feet west of Georgetown Pike to 300 feet east of Reston Ave. will not begin before December 31, 2013

Phase I: Spring 2013 to Fall 2013

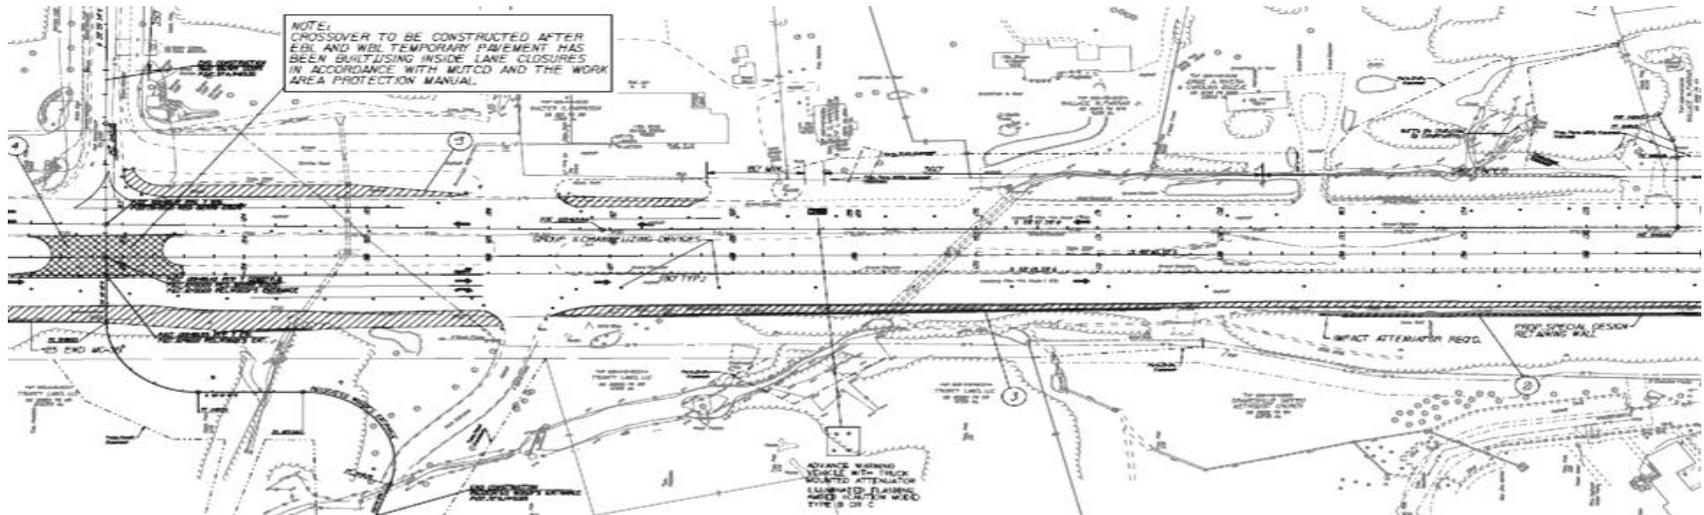


PHASE 1:

- Construct temporary pavement widening on EB & WB Rte. 7 and on east side of Georgetown Pike
- Construct new crossover for Redberry Court
- Construct Retaining Wall - EB Rte. 7

PHASE 1A

- Shift EB traffic onto Rte. 7 temporary pavement
- Build temporary pavement in median for Rte. 7 detour
- Remove existing median and construct temporary pavement at Georgetown Pike

Phase II: Fall 2013 – Fall 2014

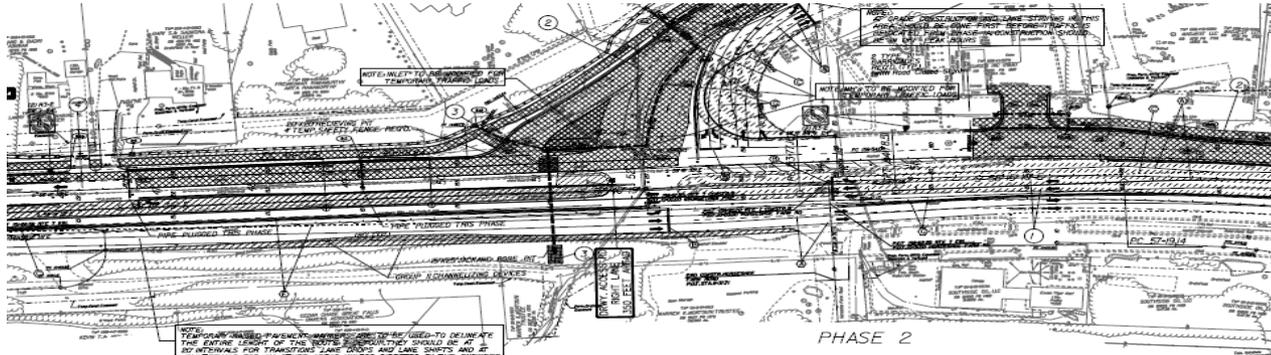

PHASE 2:

- Activate temporary signals at Redberry Court and Georgetown Pike
- Shift traffic to temporary pavement at Georgetown Pike west side
- Close the inside WB lane of Rte. 7 and shift thru traffic to outside WB lane. Local traffic detoured onto one-way service road to signal at Redberry Court
- Construct Retaining Wall on the WB side of Rte. 7


PHASE 2A:

- Maintain WB Rte. 7 Detour
- Shift WB Rte. 7 and local traffic on service road at Redberry Court

PHASE 2B


- Maintain WB Rte. 7 Detour
- Construct Rte. 7 WB lanes and connections
- Shift traffic on Georgetown Pike and construct proposed east side

Phase III: Fall 2014 to Summer 2015

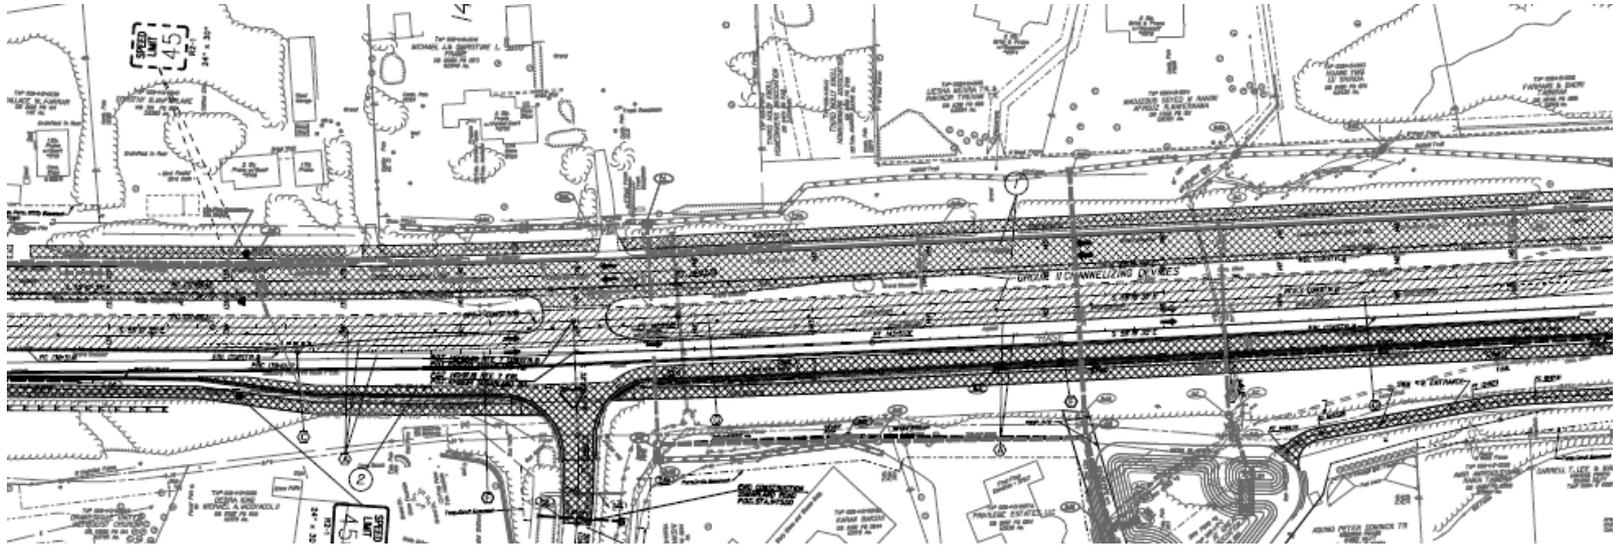

- Shift WB traffic onto newly constructed lanes
- Implement Sugarland Road detour. Shift EB traffic and construct proposed pavement
- Construct medians at Georgetown Pike and Seneca Road

Phase IV: Summer 2015 – Completion

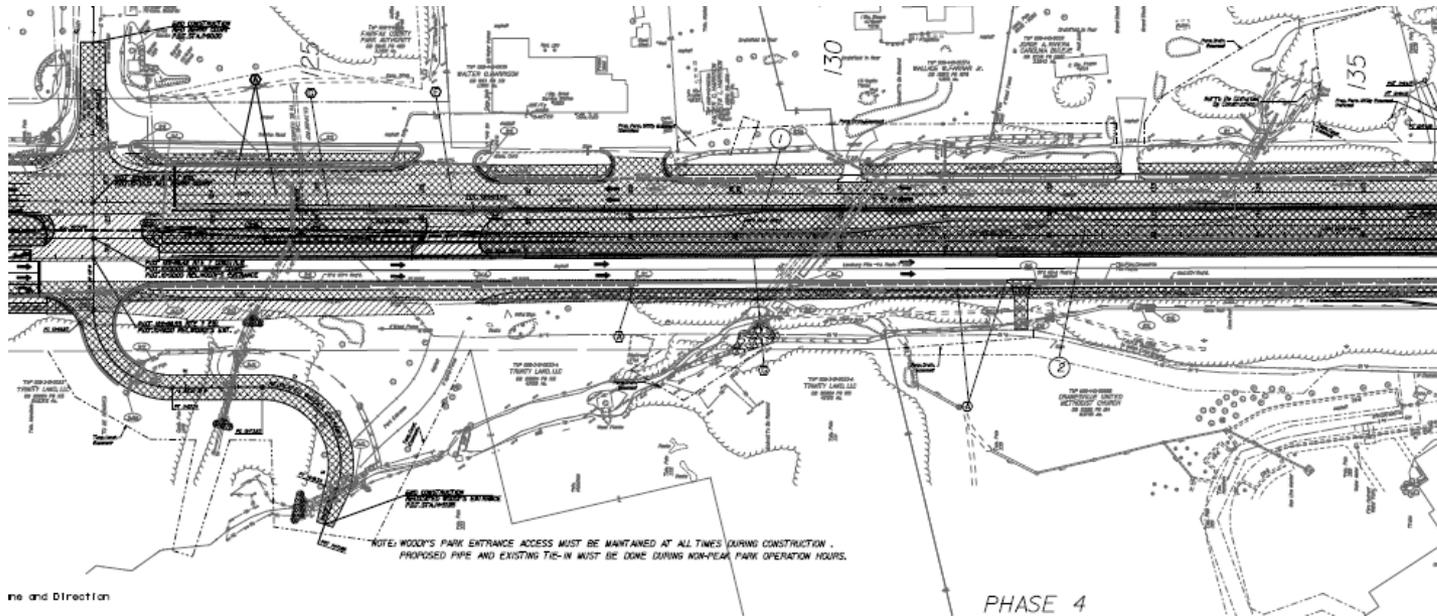

- Shift WB and EB traffic to completed lanes
- Construct inside lane widening, median and crossovers
- Final landscaping

Lane Closure Restrictions:

Lane Closures will only be permitted:


Weekday	Daytime Hours	Nighttime Hours
Monday - Thursday	9:30 AM – 3:00 PM	10:00 PM – 5:00 AM
Friday	9:30 AM – Noon	10:00 PM – 9:00 AM
Saturday	Not Permitted	10:00 PM – 8:00 AM
Sunday	Not Permitted	10:00 PM – 5:00 AM

Call VA 511 for up to date traffic information

<http://www.511virginia.org/>

Night Work

- Installation of Traffic Control Devices
- Pavement Milling
- Temporary Detour Pavement
- Pavement Striping
- Pipe Crossings

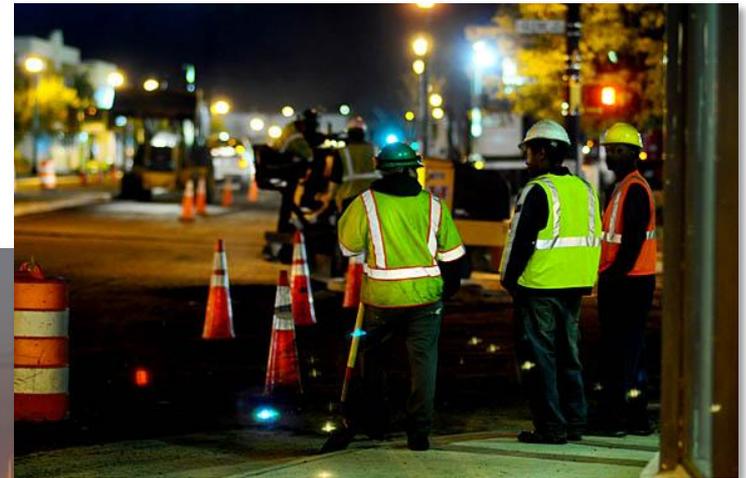

Question & Answer Session
